


YKP ERP ROADMAP & PHASE 1 MIGRATION BRIEF

HR + Finance Foundation | Spreadsheet/Data Migration | Hermez-ready Summary Layer

Prepared for internal YKP briefing and developer execution

YKP ERP + HERMEZ - ROADMAP & PHASE 1 MIGRATION

Modular ERP first. Summary-ready data. Orchestration and AI after foundation is stable.

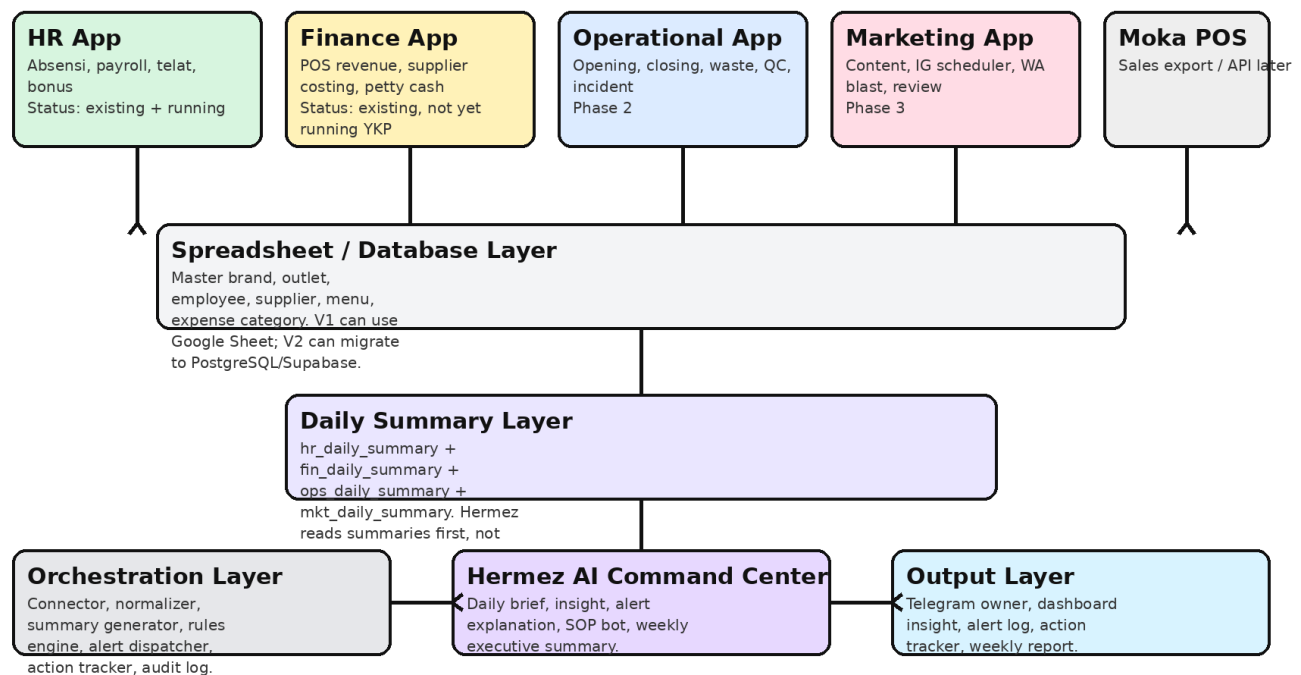

ONE-LINER: Phase 1 is not a full ERP build. Phase 1 is migration and activation of existing HR + Finance apps using real YKP data, with master data and summary sheets ready for Orchestration and Hermez.

Executive Summary

YKP will build the ERP in phases. The first phase focuses only on getting the existing HR and Finance apps running with YKP data. Operational, Marketing, Orchestration Layer, and Hermez AI come after the foundation is stable.

Module	Current Status	Phase 1 Action	Later Phase
HR App	Existing + running	Clone/migrate to YKP data, test attendance/payroll	Hermez HR insight
Finance App	Existing but not running YKP	Clone/migrate to YKP data, POS/costing/petty cash	Finance alerts, profit insight
Operational App	Visual/mockup exists	Out of Phase 1	Opening, closing, waste, QC, incident
Marketing App	Visual/mockup exists	Out of Phase 1	Content, IG scheduler, WA blast, review
Hermez AI	Not active yet	Prepare summaries only	Daily brief, alerts, SOP bot

Part 1 - Roadmap YKP ERP + Hermez

1. Project Overview

YKP wants to build an internal ERP for multi-brand F&B operations covering Funkydak, Sekarpizza, Suburbuns, Laju Kopi, and Uncle Masala. The strategy is modular: use existing apps where possible, stabilize data first, then add orchestration and AI.

2. Big Architecture

1. HR App + Finance App + Operational App + Marketing App + Moka Export

2. Spreadsheet / Database Layer

3. Daily Summary Layer

4. Orchestration Layer

5. Hermez AI Command Center

6. Owner Brief / Alert / Dashboard / Telegram

3. Build Roadmap

Phase	Name	Estimate	Main Scope
Phase 0	Audit Existing System	2-3 days	Audit HR & Finance apps, sheets, dummy data, hardcoded formulas, role access.
Phase 1	HR & Finance Migration Foundation	2-4 weeks	Clone apps, create YKP database/spreadsheets, migrate HR and Finance, pilot 1 brand/outlet.
Phase 2	Operational Dashboard V1	2-4 weeks	Opening checklist, closing reconciliation, waste log, incident/complaint, QC, ops summary.
Phase 3	Marketing Dashboard V1	2-4 weeks	Content tasks, IG scheduler, WA blast planner, campaign tracker, review monitor, marketing summary.
Phase 4	Orchestration Layer V1	2-3 weeks	Connector, normalizer, summary generator, rules, alert, action tracker, audit log.
Phase 5	Hermez AI Command Center V1	2-4 weeks	Owner daily brief, weekly summary, insight, alert explanation, SOP/Recipe bot.

4. Non-Negotiable Principles

- Do not build all modules at once.
- Start with HR and Finance because both apps already exist.
- V1 can use spreadsheet/Google Sheet, but structure must be clean and migration-ready.
- All modules must share the same master data: brand, outlet, employee, supplier, menu, expense category.
- Every module must produce daily summary sheets.
- Hermez is not the input app. Hermez reads summary and gives insight.
- Every important process must have timestamp, PIC/user, and audit log.

Part 2 - Phase 1 Migration Brief

1. Phase Name

Phase 1 - HR & Finance Migration Foundation

2. Objective

Make the existing HR App and Finance App usable for YKP data. This phase is focused on cloning, database replacement, data mapping, testing, pilot rollout, and summary preparation for future Hermez integration.

3. Scope vs Out of Scope

Included in Phase 1	Not Included in Phase 1
Audit HR and Finance apps Clone HR and Finance apps Create YKP spreadsheet/database Master data setup HR data migration Payroll rules setup Finance data migration POS/Moka import setup Supplier costing Petty cash Expense log HR + Finance summary sheets Pilot 1 brand/outlet Basic documentation and admin training	Full Operational app Full Marketing app Full Hermez AI Full Orchestration Layer Moka real-time API WhatsApp API Real-time KDS PostgreSQL/Supabase migration SOP bot AI purchasing/payroll automation Full multi-outlet rollout without pilot

4. Phase 1 Data Pack Required from Owner

File/Data	Required Contents
Master Brand & Outlet	brand_id, brand_name, outlet_id, outlet_name, address, PIC, status
Master Karyawan	employee_id, name, phone, telegram_id, brand, outlet, role, join_date, status, salary, default shift, late tolerance, bank details
Aturan Payroll	working hours, shift, late tolerance, late deduction, overtime, bonus, leave rules, payroll date
Master Supplier	supplier_id, supplier_name, category, supplied items, phone, bank, account number, status
Master Kategori Biaya	category_id, category_name, type: COGS/OPEX/CAPEX/Petty Cash, related brand/outlet
Export Moka / POS	7-30 days sales: date, outlet, gross/net sales, discount, refund, void, payment method, transaction count, item sales, cashier/shift
Petty Cash	date, brand, outlet, description, debit/top-up, credit/out, balance, receipt, PIC
Supplier Costing	date, brand, outlet, supplier, item, category, qty, unit, unit price, total, paid status, receipt, PIC
Existing App Access	testing account, HR app link, Finance app link, old database/sheet link, screenshots, known bugs

5. Recommended Spreadsheet/Database Structure

Database/File	Tabs/Tables
YKP_MASTER_DATABASE	master_brand, master_outlet, master_employee, master_supplier, master_menu, master_expense_category
YKP_HR_DATABASE	hr_employee, hr_shift, hr_attendance, hr_lateness, hr_payroll, hr_bonus_penalty, hr_daily_summary
YKP_FINANCE_DATABASE	fin_pos_revenue, fin_supplier_costing, fin_petty_cash, fin_expense, fin_unpaid_supplier, fin_daily_summary
YKP_SYSTEM_LOG	migration_log, error_log, user_activity_log

6. Developer Technical Tasks

6.1 Audit Existing Apps

- Check old Spreadsheet ID and sheet tabs.
- Check column structure and data types.
- Find hardcoded formulas or dummy brand/outlet names.
- Check role/user access and auth flow.
- List known bugs and reusable components.

6.2 Clone Apps

- Create YKP HR App Testing and YKP Finance App Testing.
- After validation, create YKP HR App Production and YKP Finance App Production.
- Do not edit old app without backup.

6.3 Replace Database Source

- Replace old spreadsheet/database source with YKP database.
- Ensure every page reads from new source.
- Ensure every form writes to new source.
- Ensure filters use YKP master data.
- Remove all dummy data from production.

6.4 HR Migration

- Import employees and shift rules.
- Setup late tolerance and deduction rules.
- Setup payroll, bonus, and penalty logic.
- Test attendance check-in/check-out.
- Generate hr_daily_summary.

6.5 Finance Migration

- Import suppliers and expense categories.
- Setup POS revenue import/export from Moka.
- Setup supplier costing, petty cash, expenses, unpaid supplier.
- Validate revenue against Moka export.
- Generate fin_daily_summary.

7. Pilot Test

Pilot should be done with 1 brand or 1 outlet for 7-14 days. Recommended options: Funkydak if YKP wants to test the most complex data, or Suburbuns if YKP wants a more stable and cleaner first pilot.

- HR attendance
- Payroll simulation
- Finance input
- Supplier costing
- Petty cash
- POS revenue
- Daily summaries
- Bug and UX feedback

8. Timeline Phase 1

Week	Focus
Week 1	Audit HR/Finance apps, create YKP database, clone testing apps, map old DB to new DB.
Week 2	Migrate HR and Finance, import employee/supplier/category data, test attendance/payroll/POS/petty cash.
Week 3	Pilot 1 brand/outlet, fix bugs, validate numbers, create HR/Finance summaries, train admin.

Week 4	Limited go-live, support, Phase 2 notes, prepare Operational App V1.
--------	--

9. Risks & Mitigation

Risk	Mitigation
YKP data is not clean	Start with simple master data; do not wait for perfection.
Hardcoded formulas in old apps	Audit all formulas and sheet references before migration.
Dummy data mixed with production	Create new production spreadsheets and remove dummy data before go-live.
Payroll mismatch	Manual test 5-10 employees before full use.
Finance mismatch with Moka	Reconcile daily revenue with Moka export.
Scope creep	Phase 1 is HR + Finance only. Operational, Marketing, Orchestration, Hermez are later.

10. Definition of Done - Phase 1

- ☐ HR App reads YKP data.
- ☐ Finance App reads YKP data.
- ☐ Master brand/outlet/employee/supplier data is clean.
- ☐ Attendance works.
- ☐ Payroll simulation works.
- ☐ Finance revenue, supplier costing, petty cash, and expenses work.
- ☐ HR daily summary exists.
- ☐ Finance daily summary exists.
- ☐ Pilot 1 brand/outlet runs for at least 7 days.
- ☐ No dummy data mixed with production.
- ☐ Basic documentation exists.
- ☐ Admin can input data independently.

FINAL NOTE: Phase 1 must stay focused. The goal is HR + Finance running with real YKP data, not building the full ERP yet.
